
# Abitibi River Forest Appendix 1: Form for Submission of Information on a Proposed Crossing

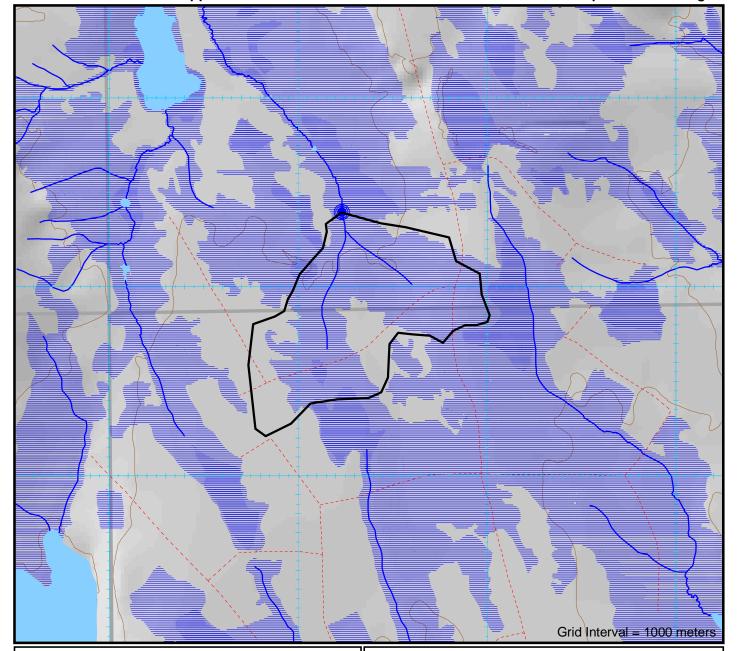

### **Watershed Characteristics**

0.82 km<sup>2</sup> Watershed Area: 0.00 km<sup>2</sup> Lake Area: 0.02 km<sup>2</sup> Swamp Area: 0.02 km<sup>2</sup> Retention Area: 2.55 % Retention Factor: 0.00 Base Class: Watercourse Type: Permanent

# **Crossing Location Characteristics**

Evaluation ID No.: A3304 Geographic Township: Hoblitzell

UTM Coordinates (NAD83): 568232E, 5478395N

Road Type

Stream Gradient: 0% Slope > 30% (17°): NO

Installer Experience : As Per Approved Implementation Toolkit



| Proposed Structures              |                |                      |                 |  |
|----------------------------------|----------------|----------------------|-----------------|--|
|                                  | Structure 1    | ucture 1 Structure 2 |                 |  |
| Structure Type                   | Culvert        | Ice                  | Portable Bridge |  |
| Design Flow                      | Q10            | Q2                   | Q25             |  |
| Fill Material                    | Pit Run Gravel | Snow and Ice         | Pit Run Gravel  |  |
| Dates for In Start<br>Water Work | July 16        |                      | July 16         |  |
| (if required) Finish             | August 31      |                      | August 31       |  |
| Removal Timeframe                | <2 Years       | By March 31st        | <7 Years        |  |

Calculations performed by First Resource Management Group (FRMG). Neither Abitibi River Forest Managment Inc., nor FRMG guaratee the accuracy of any information presented on this form. Coordinates and map are UTM projection, Zone 17 NAD83 datur

Shaded Area for | ARFMI Road Previously Used Crossing Evaluation Office Use Only Network No. Crossing ID Reference Number

Publication Date: December 19, 2023

Fisheries Operational Management Zone (OMZ): Abitibi River Forest - S.F.L. # 551832

Standard for Self-assessed Water Crossing Construction, Removal and/or **Proponent:** 3 Nations Logging LP Decommissioning: Conditions of standard not met for first structure. See red text. c/o P.O. Box 867

New Liskeard, Ontario Previous Assessment Year (incl. SA): 2024 P0J 1P0 SAR species likely to be impacted: NO (705) 680-0033 NO Preconstruction photos available:

Plan Term: 2022-2032 NO Within 500m of Brook Trout stream: AWS Year: 2024-25

| Culvert Design Options |  | <b>Q</b> <sub>25</sub>    | <b>Q</b> <sub>10</sub> | $Q_5$                     | <b>Q</b> <sub>2.33</sub>  |
|------------------------|--|---------------------------|------------------------|---------------------------|---------------------------|
|                        | Design Flow  | 0.000 m <sup>3</sup> /sec | 0.000 m³/sec           | 0.000 m <sup>3</sup> /sec | 0.000 m <sup>3</sup> /sec |
|                        | 1 Round  | 450mm                     | 450mm                  | 450mm                     | 450mm                     |
|                        | 2 Round  | N/A                       | N/A                    | N/A                       | N/A                       |
|                        | 3 Round  | N/A                       | N/A                    | N/A                       | N/A                       |
|                        | 1 Arch (BxD)   | 450x340mm                 | 450x340mm              | 450x340mm                 | 450x340mm                 |
|                        | 2 Arch (BxD)   | N/A                       | N/A                    | N/A                       | -                         |
|                        | 3 Arch (BxD)   | N/A                       | N/A                    | N/A                       | -                         |
|                        | Required Opening for bridges is calculated as per the Crown Land Bridge Management Guidelines. |                           |                        |                           |                           |

### **Conditions on Culvert Design Options**

- · Initial Fisheries Review based on one pipe. Two or more pipes requires a re-assessment.
- Round culvert calculations assume 10% fill. For 20% fill, increase diameter to next highest standard diameter.
   For 40% fill, use a round culvert diameter of the Base distance of the corresponding Arch style culvert.

### **General Standards**

- No watercourse realignment, nor use of explosives is permitted.
   Minimize loss or disturbance to riparian vegetation. Restrict removal of riparian vegetation to the disturbance footprint required for construction, maintenance and decommissioning of the water crossing.
- Install erosion and sediment control measures prior to commencement of construction or decommissioning to prevent release of sediment or other deleterious substances into watercourse.
- Fill material placed below the normal high water mark must be erosion-resistant and/or protected from erosion. • Direct storm water runoff from bridge decks, side slopes, road approaches and ditches away from the watercourse
- and into a retention pond or vegetated area.

  Ensure erosion and siltation in ditch lines adjacent to the watercourse crossing approaches are controlled using sediment traps such as rock/soil dams or log jams as site conditions warrant.

  Do not block or impede the free passage of water and fish at any time of year up and down stream,
- with the exception of potential and temporary blockage due to water crossing construction/decommissioning activities. • Abide by fisheries in-water timing windows in the approved FMP and/or forest management guides.
- Where fishery communities are not well documented, the most restrictive in-water timing window must be used. • Complete all in-water construction and decommissioning activities in an uninterrupted fashion and in an appropriate
- timeframe to minimize potential for site disturbance.

  If installation requires inwater work, do not locate within 100m of spawning or sensitive fish habitat eg. rapids, riffles, known overwintering areas.
- Maintain machinery free of fluid and fuel leaks. Wash, refuel and service machinery at least 30m from watercourse. Store fuel and other materials for machinery a minimum of 30m from the watercourse
- · Operate machinery on land with tracks/wheels above the normal high water mark, or on ice in a manner that avoids disturbance to the banks of the watercourse and adjacent riparian vegetation areas.
- Remove all debris from construction and decommissioning work from the site following completion of the undertaking.
- If machinery fording is required, limit to a one-time event (over and back) per piece of equipment essential to implementating the project, and only if using an existing crossing at another location is not available or practical.

  If minor rutting is likely, watercourse bank and bed protection methods (e.g., swamp mats, pads) are to
  - be used provided they do not constrict flows or block fish passage; Grading of the watercourse banks for the approaches is not permitted;
- If the watercourse bed and banks are steep and highly erodible (e.g., dominated by organic materials and silts)
- and erosion or degradation is likely, use a temporary crossing structure or other practice to protect them; • The one-time fording must adhere to the appropriate in-water timing windows; Fording must occur under low-flow
- conditions and not when flows are elevated due to local rain events or seasonal flooding.

- · All calculations are for projecting ends. Total pipe length normally not to exceed 20m.
- All calculations assume a Headwater Depth of 1.0.
- MP = Multi-Plate (i.e. SPCSP)

## Standards for Single, Small Closed-Bottom Round Culverts

- This standard applies to single, round, corrugated, closed-bottom steel, aluminum, or plastic culverts less than or equal to 1200mm in diameter that do not require site-specific engineering approval per MNRF's Crown Land Bridge Manual.
- This standard only applies if the project does not:
- Replace an existing open-bottom crossing (e.g., clear span bridge, arch culvert);
- Replace an existing closed-bottom culvert larger in diameter than that being installed; or - Involve the installation of more than one closed-bottom culvert at the crossing location.
- Locate, design and construct to minimize likelihood of ongoing outlet scour, culvert undermining or erosion of fill in order to provide stable, non-perched culverts that provide for fish passage
- Do not locate on meander bends, braided streams, or any other area inherently unstable that may result in alteration of natural stream functions or erosion and scouring of the structure.
- Size to a minimum Q25 design flow. If an unmapped stream is encountered and proper analysis cannot be completed to determine Q25, size to ensure it spans from bank to bank.
- Do not install where channel slope at crossing location is of a gradient greater than 2.0%.
- Do not install where slope of road approaches or either bank approach is greater than 30% (17°).
- · Locate where culvert can be embedded below grade of stream bed.
- · Use site-specific mitigation measures to ensure no ongoing erosion of fill. As a minimum:
- Stabilize both inlet and outlet ends with appropriately sized non-erodible material;
- Rock used is clean, free of fine materials and of sufficient size to resist peak flood events;
- Place rock at original bank grade to ensure no infilling or narrowing of watercourse;
- Fill material placed below normal high water mark must be erosion resistant and/or protected from erosion.
- The Forest Management Guide for Conserving Biodiversity at the Stand and Site Scales refers to the normal high-water mark as the edge of vegetation communities capable of providing an effective barrier to the movement of sediment.

  • Do not locate within 100 metres of fisheries spawning or sensitive habitat.
- Do not locate within 500 metres of any brook trout spawning or upwelling greas.
- Do not locate on watercourses that flow into, and are within 500m of, known naturally reproducing brook trout lakes.
- Mix of size, length, slope & drainage area must not increase flows to consistently & predictably impede fish passage.
- Install under low-flow conditions and not when flows are elevated due to local rain events or seasonal flooding.
- Both interior and exterior of culverts must be corrugated to ensure structural stability and facilitate fish passage
- The grade of the culvert must reflect the grade of the natural watercourse bed.
- Compact backfill adequately around the culvert. Use only dean sand or gravel and compact around the culvert in layers.
- Length of culverts must permit banks to be sloped at an angle of 2:1 or a stable angle of repose for the materials used.

# Self-assessed. Follow conditions of appropriate standard(s).

# MNRF Appendix 2: Biologist Risk Evaluation

Concerns and Conditions on Construction

Watershed Thermal Code: UF

MNRF Assigned Thermal Code at Crossing


|                           | Structure 1 | Structure 2 | Structure 3 |
|---------------------------|-------------|-------------|-------------|
| Risk Evaluation:          | LOW         | LOW         | LOW         |
| Site Inspection Required: | NO          | NO          | NO          |


| A DIWINI DIAME                         |
|--|
| ABITIBI RIVER<br>Forest Management Inc |

| <b>ΔRFMI</b> Cross  | ing Installation I                           | Renort                                 | 1.16  | Only certifie      | ed inspectors are allowed to condu                                      | ct Forest Operations Insper      | ctions for submi |
|---|--|--|---|--------------------|---|----------------------------------|------------------|
| TIBI RIVER Management Inc                                   | ing marananan                                | (Must be com                           | pleted for each crossing location)  |                    | * 'As Built' Culvert I  | nstallation Measuren<br>(meters) | nents            |
| Shareholder:  |  | Block ID:                              |   | <b> </b>           | Installed Diameter :  |                                  |                  |
|   |  | Road Names                             |   | CULVERT            | Structure Length :  |                                  |                  |
| Contractor:   |  | Road Name:                             |   |                    | Road Width :  |                                  |                  |
| TE CONDITIONS ENCOUNTE                                      | RED  |  |   | O                  | Depth of Cover:   |                                  |                  |
| Crossing Located By:  |  | Date Measurements Taken:               |   |                    | Water Depth in Pipe :   |                                  |                  |
|   |  |  |   |                    | Number of Culverts :  |                                  |                  |
| Stream Measurements   |  |  | Foundation Soil Description :   |                    | Spacing Between Pipes :   |                                  |                  |
| (meters)  | <u>l</u>                                     |  | Sand Muck   |                    |   |                                  |                  |
| Flood Plain Width : A                                       |  | <b>徐</b> 徐                             | Silt Rubble   |                    | * 'Ac Ruilt' Bridge I   | nstallation Measurem             | ments            |
| Bankful Width : B   |  | A ———————————————————————————————————— | Clay Gravel   |                    |   | (meters)                         | IICIII2          |
| Channel width : C   | F E  | <u>v</u>                               | Channel Type:   |                    | Bridge length :   | G                                |                  |
| Depth - 25% of Channel : D (I)                              | D (I)  | † †<br>) D(c) D(r)                     | Ephemeral Ephemeral   |                    | Clear Opening Width :   | Н                                |                  |
| Depth - 50% of Channel : D (c)                              | Notes:                                       |  | Intermittent  |                    | Freeboard (min 0.5m) :  | I                                |                  |
| lepth - 75% of Channel : D (r)                              |  |  | Permanent   | 99                 | Flood Rise :  | J                                |                  |
| Depth - Bankful Flow : E                                    |  |  | ADDIM N. C D I I  | BRIDGE             | Fill Height :   | K                                |                  |
| Depth — Floodplain : F                                      |  |  | ARFMI Notification Provided : (ARFMI Advised- 'Change to Operation' made) |                    | Left Slope Length :   | L                                |                  |
| Stream Velocity : m /s                                      | ес   |  | FRI Incorrect   |                    | Left Slope Rise :   | M                                |                  |
|   |  |  | Unmapped  |                    | Right Slope Length :  | N                                |                  |
|   |  |  |   |                    | Right Slope Rise :  | 0                                |                  |
| STALLATION CONDITIONS                                       |  | 1                                      |   |                    | Crib Width :  | P                                |                  |
| tallation Supervised By:                                    |  | Date of installation:                  |   |                    | Crib Height :   | R                                |                  |
|   |  |  |   |                    |   |                                  |                  |
| ossing Permanency :Refer to Structure Removal Timeframe s   | pecified in AWS 4 and 5  Month / Year        |  | Fracian Proportion and Control /V   | Verific            | ation:<br>I have confirmed that the final a                             | rossing condition                | Water C          |
| Permanent Temporary Deco                                    | mmissioned Date:                             |  | Erosion Prevention and Control (X): (Indicate applicable measures taken)  |                    | satisfies the mandatory water cro<br>will not impede future transfer of | ssing standards and              | lns No           |
| ote: Measurements (*) must be included for all              | ed Removal Date:                             | Stable slopes on st                    | tream banks and drainage ditch banks                                      | Notes              | ·   |                                  | 7 🔲 Co           |
| Uctores which remain in prace beyond date of inspection     |  | _                                      | Course, clean rock to high water mark                                     | I Note:            | <b>J</b> .  |                                  | En Tir           |
|   | ctual Crossing Location on Stream Segment ): | Re-vegetate or seed s                  | slopes (stream banks and ditch banks)                                     |                    |   |                                  | Cu<br>Se         |
| Bridge Record Form submitted (i.e. MNR /ARFMI)              |  |  | Divert drainage ditches to green belt                                     |                    |   |                                  | No               |
| New Crossing Type: Structure Description                    |  | _                                      | Line drainage ditches with rock   |                    |   |                                  | No.              |
| New Crossing Type: Structure Description  Box Culvert Steel | n: Type of Fill:  Sand                       | Use rock weirs in                      | drainage ditches to impede water flow                                     |                    |   |                                  | No Ad            |
| Arch Culvert Plastic  | Gravel                                       |  | filter cloth on upstream side of culverts                                 |                    |   |                                  | Dro              |
| Round Culvert Wood  | Rock Rubble                                  |  | obing or stripping of ground vegetation                                   |                    |   |                                  | Cro              |
| Portable Bridge Concrete                                    | Other  |  | of ice if fill is used for Winter Crossings)                              |                    |   |                                  | Ro               |
| eel Stringer Bridge Ford (Engineered)                       |  | oso mior cioni (on top o               | Other:  | Note: All o        | of the above activities must be che                                     | cked. 🗸 - Verified to be         | e within accepta |
| Winter Snow Pack  |  |  | Ulliel:   | I certify that the | activities inspected are fully complia                                  | nt based on an Siana             | nture.           |

FOIP Report Number : FOIP database

Inspector Name:



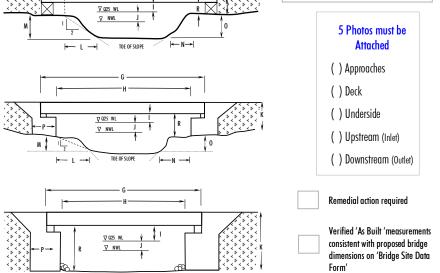

| Verification :  | Water Crossing Activity (X):   |
|---|--|
| I have confirmed that the final crossing condition                    | Water crossing location same as AWS submission   |
| satisfies the mandatory water crossing standards and                  | Installation of culvert and size same as described in AWS water shed calculations.                                       |
| will not impede future transfer of responsibility                     | No sediments or woody debris left in water body or streams   |
| Natari  | Construction materials removed from site   |
| Notes:  | Embankment sloped properly (e.g. 2:1) with no possibility of slumping  |
|   | Timing restriction met   |
|   | Culvert properly installed (i.e. refer to FMP Standards )  |
|   | Sediment Control Plan in AWS followed  |
|   | No Erosion or Sedimentation present (e.g. filter cloth used to prevent material from entering waterway)                  |
|   | No signs of equipment or machinery in stream (i.e. culvert installed before equipment progresses past crossing)          |
|   | Coarse clean rock used on all culvert crossings  |
|   | Natural vegetation protected   |
|   | Additional measures used to prevent erosion (e.g. seed, filter cloth, rip rap etc.)                                      |
|   | Drainage ditches properly installed  |
|   | Crossing removed before March 31 unless left for silviculture activities   |
|   | Road right of way width through unallocated stands , no larger than FMP requirement                                      |
|   | Road right of way width through AOC's (reserves), no larger than FMP requirement   |
| Note: All of the above activities must be checked. 🗸 - Verified to be | within acceptable limits 🗶 - Outside of acceptable limits. Refer to comments for additional details N/A — Not applicable |

inspection appropriate to support this decision.

Date: \_\_\_

Bridge Used (Identification #):
